



Product & Delivery Plan

An internal platform to manage the lifecycle of government competitions and contracts – from order creation to contract closeout – with follow-up of project and contractor execution, payments and reports.

The internal operating system around Etimad: it turns manual work into an automated, AI-assisted workflow under human oversight, and complies with the Essential Cybersecurity Controls (ECC).

Version

2.0 – Edited

Date

June 2026

Classification

Confidential

Prepared by

**Kareem Adel
Mohammed**

»» At a glance

The product and plan headline numbers on one page

10

competition lifecycle stages

18

contract lifecycle actions

~13

roles & permissions (RBAC)

108

cybersecurity controls (ECC) across 4 domains

145

delivery tasks in the plan

24

weeks – reference schedule

What does Tanfeeth offer, briefly?

- **One clear path** from order creation to contract closeout, with precise permissions and a complete record of every action.
- **Integrates with Etimad** (does not replace it) and owns the post-signature world: contractor, payments, warnings, acceptance.
- **An AI assistant** that suggests and explains, while the final decision always stays with the responsible user.
- **Security commitment** to the Essential Cybersecurity Controls (ECC) and in-Kingdom data residency.

★ **The core idea:** Tanfeeth is not just a dashboard – it is a complete operating system connecting the entity with the contractor, committees, departments and oversight bodies in one governed, audited system.

Contents

A concise, direct version for approval and delivery

1 Executive summary

2 Product scope & boundaries

3 Users & permissions

4 Core workflow

5 Post-signature contract management

6 End-to-end scenario

7 AI, reporting & integrations

8 Core rules & requirements

9 Delivery scope & priorities

10 Timeline & delivery plan

11 Dependencies & risks

12 Decisions required

13 Cybersecurity & protection (ECC)

14 User stories

15 Scenarios in detail

16 FAQ

How to read: Sections 1-8 explain the product and its controls. Sections 9-12 are the delivery and approval plan. The document is followed by **Appendix A – the Detailed Task Register**, breaking down each task by category (Infrastructure / User Interface / Systems Integration / AI / Deployment & Ops / QA Testing / Design / PM / Security), description, dependencies, status and estimated hours.

» 1. Executive summary

What does Tanfeeth provide?

Tanfeeth is an internal platform that helps a government entity manage competitions, contracts and projects in one clear path, with precise permissions and a complete record of every action.

It integrates with Etimad and does not replace it. Etimad handles tendering, receiving offers and award, while Tanfeeth manages the entity's internal work, then follows the contract and project after signature.

Key value

- **Clear governance:** an order or contract changes state only through an approved, authorized action.
- **Full follow-up:** the platform shows project status, delays, letters, payments and contractor obligations.
- **Audit trail:** the system records who performed an action, when, and the state before and after it.
- **AI assistant:** the system suggests the right action and explains why, and the final decision stays with the responsible user.

Core principle: the AI does not automatically approve any financial, contractual or regulatory decision.

2. Product scope & boundaries

The relationship between Tanfeeth and Etimad

Etimad platform	Tanfeeth platform
● Publishing the competition and receiving offers. ● Award procedures. ● May be the signing surface and source of contract data.	● Order & kraasa preparation, internal approvals and committees. ● Internal offer analysis and reflecting the signed contract. ● After signature: project, contractor, letters, payments, amendments, acceptance.

The gap Tanfeeth fills: everything that comes after award and signature – which Etimad does not cover.

In scope

- Managing orders, competitions, contracts and projects.
- Approval workflow, assignment, signing and official correspondence.
- Contractor portal, progress tracking and contract-action management.
- Reports, dashboards, audit log and required integrations.

Out of current scope

- Replacing Etimad or duplicating its official functions.
- Executing AI decisions without human approval.
- Blockchain, voice assistant and advanced capabilities before the core is complete.

3. Users & permissions


Who uses the platform?

User	Main responsibilities	Access scope
Contracts & procurement dept	Manage the competition, contract, actions and correspondence.	By department and permission.
Requesting / supervising dept	Create the order, follow execution, verify contractor performance.	Their projects and orders.
Finance dept	Budget, commitment, payments and guarantees.	Authorized financial data.
Higher management	Final approval, escalation and signing.	Decisions and executive dashboards.
Contractor	Review the contract, update progress, submit requests, reply to letters.	Their contracts only.
Oversight	Review compliance and the audit log.	Read & audit only.
Platform admin	Manage users, roles and workflow settings.	System administration without crossing tenant isolation.

Permissions rule: every user sees and does only what their permissions allow, and every assignment or delegation is recorded in the system.

4. Core workflow

From order to project start

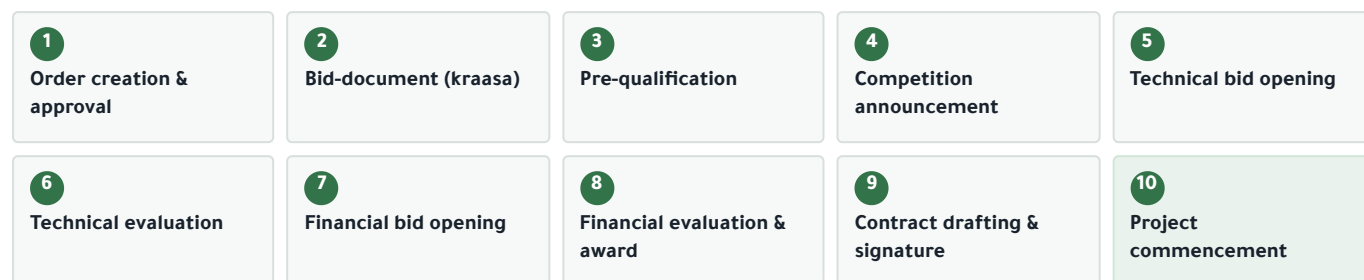

Configurable rule: if the budget exceeds the set threshold, the system splits the technical document from the financial one. Commencement also differs between supply and maintenance projects.

» 5. Post-signature contract management

The product's core focus

After the contract is signed, actual execution follow-up begins. The system shows milestones, planned-vs-actual, the BOQ, payments, letters and decisions.

Priority actions in the core

Group	Actions	Effect
Start & follow-up	Commencement, site handover, suspension, resumption.	Update project status and duration.
Default handling	Warning, final warning, withdrawal of works.	Document the breach and escalate.
Contract amendment	Variation order, extension.	Adjust scope, value or duration.
Financial rights	Payments, assignment, guarantees.	Record financial and guarantee effects.
Closeout	Preliminary acceptance, final acceptance, termination.	Close the contract and evaluate the contractor.

Correspondence control: every external letter obtains a reference number and date before it is sent, and is logged with approvals and attachments.

» 6. End-to-end scenario

Delay, warning, withdrawal of works, and the completion contract

1

The **project dashboard** shows the contractor falling behind schedule.

2

The **AI** suggests issuing a warning and explains the reason.

3

Human decision: the supervising department reviews the suggestion and approves, edits or rejects it.

4

The system generates the **warning letter**, obtains a reference number, then sends it.

5

The **contractor replies inside the platform** within the set window.

6

Check: the department reviews the reply – if unresolved, a **final warning** is issued.

7

If the breach continues, **withdrawal of works** is approved per permissions.

8

The system creates a **completion contract** linked to the original and loads the remaining works into it.

9

All steps and decisions are recorded in the **audit log**.

Core acceptance criterion: this scenario runs end-to-end on a test contract, with permissions, correspondence, audit and completion-contract linking.

7. AI, reporting & integrations

Capabilities that support operations

Artificial intelligence

- Suggest the next action with its reason and sources.
- Alert the user to delay and compliance risks.
- Summarize contracts, letters and documents.
- Every impactful decision requires explicit human review and approval.

Dashboards & reports

- Contract-manager dashboard: active, defaulting and near-expiry contracts.
- Higher-management dashboard: commitments, performance, risk and compliance.
- Contractor dashboard: obligations, updates, requests and letters.
- Reports exportable as PDF, Excel and CSV.

Priority integrations

Priority	Integration	Purpose
Critical	Etimad, Nafath, Ministry of Finance	Competitions, identity and budget.
High	E-signature, GOSI	Document signing and supplier verification.
Medium	ERP/CRM, WhatsApp Business	Sync and notifications.

8. Core rules & requirements

Controls that must not be bypassed during delivery

Area	Rule
Workflow	Every state change happens through an approved, authorized transition.
Audit	Every impactful action is recorded with the actor, time and before/after state.
AI	No impactful decision executes without human review and approval.
Permissions	Access is based on role, permission, entity and contract.
Correspondence	No external letter is sent without a reference number and date.
Integrations	The platform stays consistent with official data sources.
Security	In-Kingdom hosting, encryption, tenant isolation and NCA/CST compliance.
Localization	Arabic and English, RTL, Hijri and Gregorian calendars, and SAR.
Configuration	Approval chains, thresholds and rules are set from configuration, not custom code.
Definition of done	A feature is not done until it is tested end-to-end.

» 9. Delivery scope & priorities

What is delivered first?

Package	Scope	Done criterion
Operational core	Identity & permissions, tenant isolation, workflow, audit, documents, correspondence, contractor onboarding.	Run a test contract with correct permissions and a complete log.
Contract execution	Contractor portal, commencement, progress, BOQ, warnings, withdrawal of works.	The end-to-end scenario passes.
Full cycle	Committees, evaluation, award, signature, financial actions, closeout, contract linking.	Manage a full cycle from order to closeout.
Integration & intelligence	Live integrations, management dashboards, risk, compliance, advanced analytics.	Integrations and agreed KPIs operating.

Epic map at a glance

E01–E07 platform foundations, E08–E12 pre-award & signature, E13–E18 contract & contractor execution, E19–E20 intelligence & reporting, E21–E22 integrations & localization.

10. Timeline & delivery plan

A reference plan over 24 weeks from start date

Planning assumption: weeks count after scope approval, team availability and integration environments. The schedule is re-baselined after the kickoff workshop.

Phase	Deliverables	1-4	5-8	9-12	13-16	17-20	21-24
Setup & design	Scope approval, workflow design, integration plan, acceptance criteria.	Run					
Platform foundations	Permissions, tenant isolation, audit, documents, correspondence.	Start	Run	Approve			
Operational core	Contractor onboarding, portal, commencement, progress, warnings.		Start	Run	MVP		
Full cycle	Committees, award, signature, remaining contract actions, closeout.			Start	Run	Approve	
Integrations & dashboards	Live integrations, management reports, risk.				Start	Run	Launch
Testing & launch	Full testing, pilot migration, training, phased launch.					Test	Launch

Key milestones

Milestone	Reference date	Approval condition
M0 – Design approval	End of week 4	Scope, workflow and integrations approved.
M1 – Foundations ready	End of week 8	Permissions, audit, documents and correspondence working.
M2 – Operational core (MVP)	End of week 16	The delay → completion-contract scenario passes.
M3 – Full cycle complete	End of week 20	Run the cycle from order to closeout.
M4 – Phased launch	End of week 24	Testing, training and support plan passed.

11. Dependencies & risks

What could affect the schedule?

Critical path

E01 → E03 → E05 → E13 → E14 → E15 → E16 → E17

The core depends on permissions, the workflow engine and correspondence being ready before building the contractor portal and execution actions.

Risk	Impact	Proposed action
Delay of official integration interfaces	Delays signing, sync and verification.	Use sandboxes and clear integration contracts until live links are available.
Approval chains not approved	Blocks workflow design.	Early decision workshop and an approved first configurable version.
Scope creep during delivery	Delays the core and launch.	Freeze the MVP scope and manage new requests as a later phase.
Unclear guarantee/payment data	Financial and operational risk.	Approve the data model and policies with finance before phase three.
Poor data quality	Inaccurate reports and recommendations.	Validation rules, data cleansing and continuous quality metrics.

12. Decisions required

Decisions to settle before approving the final plan

1. Approve the MVP scope boundaries and deferred features.
2. Approve the approval chains for each contractual action.
3. Define the supervising department's role and its relation to the requesting department.
4. Define the permissions of oversight, the platform admin and the entity admin.
5. Define the source of reference numbers for official correspondence.
6. Approve the contractor identity and commercial-registration verification method.
7. Approve the guarantees, payments and retention model.
8. Confirm integration readiness, owners and test environments.
9. Approve the team and the start date of the 24-week plan.

Next step: hold a kickoff workshop to approve the above decisions and convert the reference schedule into a dated plan distributed across teams.

»» 13. Cybersecurity & protection

Compliance with the Essential Cybersecurity Controls (ECC-2:2024) of the National Cybersecurity Authority

Tanfeeth complies with the Essential Cybersecurity Controls (ECC-2:2024): four main domains, 28 subdomains and 108 controls. Responsibility splits into controls the **platform implements**, **organizational** controls owned by the entity (the cybersecurity function), and **shared** controls with the cloud hosting provider.

Shared responsibility principle: Tanfeeth implements the technical controls in the platform and enables the entity to demonstrate compliance, while governance, policies, awareness and audit remain the entity's responsibility, and data-center security is the responsibility of the approved in-Kingdom hosting provider.

Domain (ECC)	What Tanfeeth implements	Responsibility
1 – Cybersecurity Governance	Enabling policies, roles, the risk register and audit inside the platform.	Entity + Platform
2 – Cybersecurity Defense	Identity & MFA, encryption, network & email security, vulnerability management, monitoring (SIEM), web protection (WAF), data protection.	Platform
3 – Cybersecurity Resilience	Backup, recovery, continuity plan and RTO/RPO objectives.	Platform + Hosting
4 – Third-Party & Cloud Computing	Supplier assessment, in-Kingdom data residency and the shared-responsibility model with the cloud provider.	Platform + Provider

1 · Cybersecurity Governance

Policies · Roles · Risk · Audit · HR · Awareness

2 · Cybersecurity Defense

Identity & MFA · Encryption · Network · Email · Vulnerabilities · SIEM · WAF

3 · Cybersecurity Resilience

Backup · Recovery · Continuity · RTO/RPO

4 · Third-Party & Cloud Computing

Supplier assessment · Data residency · Shared responsibility

What the platform builds (technical controls)

- Data encryption at rest/in transit and key management; multi-factor authentication (MFA); precise permissions, least privilege, segregation of duties and privileged-access management.
- Tamper-evident audit log and continuous monitoring via SIEM; tenant isolation and in-Kingdom data residency.
- Web application firewall (WAF), HTTPS and multi-tier architecture; a secure development lifecycle (secure coding, vulnerability scanning, penetration testing).
- Backup, recovery and continuity plan; cybersecurity incident management, response and reporting to the authority.
- Email protection (SPF/DKIM/DMARC), network protection (IPS and DDoS protection) and vulnerability/patch management.

Entity responsibility (organizational controls)

- Cybersecurity strategy and policies, risk management, awareness and training.
- Cybersecurity in human resources, periodic audit and ECC self-assessment, and physical security.

Link to the plan: task-level details for these controls are in **Appendix A – Track S (Cybersecurity & Protection)**, and the alignment is updated with every release of the controls.

14. User stories

What each user wants from the platform – “As a... I want... so that...”

Requesting / supervising department

Requesting dept I create a project order with all FR-WF-001 fields and attachments and submit it, **so the procurement journey can start.**

Supervising dept I track the contractor's progress and milestones, **so I catch delays early.**

Requesting dept I initiate the preliminary and final acceptance certificates, **so the contract closes formally.**

Supervising dept I initiate the commencement request after the contract is signed, **so execution actually begins.**

Supervising dept I verify the contractor's replies to letters, **so I decide whether to escalate.**

Requesting dept I evaluate the contractor after execution, **so the supplier reliability index is fed.**

Contracts & procurement

Contract manager I create the kraasa and assign it to staff while keeping oversight, **so work distributes without losing control.**

Contract staff I create the contract data from approved drafts or import it from Etimad, **so the contract is reflected in the platform.**

Contract manager I link the completion contract to the original on withdrawal, **so another contractor finishes the remaining works.**

Contract staff I issue the award letter and letter of intent, **so the award is formalized.**

Contract manager I trigger contract actions through a gated workflow, **so every step is documented and audited.**

Contract staff I invite the contractor to register after signature, **so they can be followed inside the platform.**

Finance

Budget head I confirm the budget and apply the document-split rule, **so the documents are correctly structured.**

Finance I manage payments against the BOQ and budget availability, **so payments are controlled.**

Finance I confirm the final commitment before award approval, **so commitments don't exceed the budget.**

Finance I manage initial and final guarantees and their renewal, **so they stay valid.**

Higher management, oversight & platform admin

Higher management I approve, sign and escalate decisions, **so transactions proceed with governance.**

Oversight I view the compliance dashboard and audit log, **so I verify compliance.**

Higher management I view a strategic dashboard of risk, performance and compliance, **so I decide based on data.**

Platform admin I manage users, roles and workflow settings, **so the platform matches the entity's structure.**

Contractor

Contractor I accept the invitation and register, and my account is linked to my commercial registration and contract, **so I can work inside the platform.**

Contractor I review, sign and download my contract, **so contracting is completed electronically.**

Contractor I initiate a request (extension/value change), **so it enters the entity's gated workflow.**

Contractor I submit progress updates with images and video, **so the works are followed in real time.**

Contractor I reply to warning/dues letters inside the platform, **so my reply is recorded before escalation.**

Committees & AI

Committee member I enter evaluation scores and sign the reports, **so qualification, opening and evaluation results are approved.**

Technical evaluator I receive AI-suggested scores with explanations, **and the committee makes the final decision.**

Any user I receive a next-action recommendation with its reason, **so I decide quickly while the decision stays mine.**

15. Scenarios in detail

Covering every main and exceptional path

1 · Order creation & approval BR-01

Requesting dept creates the order → Head approves → Finance confirms the budget and applies document split above the threshold → Higher management approves. **Alternatives:** return-with-comment or reject-with-reason.

2 · Commencement – supply vs maintenance BR-02

Supply: commencement request → confirm → commencement letter → sign → reference number.

Maintenance: adds a site-handover minute, the site committee and a cover letter.

3 · Default & withdrawal of works Critical

Delay detected → AI suggestion → human approval → warning letter (with reference) → contractor reply → final warning → withdrawal → **completion contract** linked to the original. (Detail in section 6.)

4 · Contract variation

Change request (value/duration/terms) → review & approval → bid examination if needed → signing → variation letter with reference → BOQ update.

5 · Extension, suspension & resumption

Request → approval → letter (extension/suspension/resumption) with reference → update project duration and status, with guarantee-validity check.

6 · Payments & dues

Payment due against the BOQ and budget availability → approval → dues letter → record the financial effect.

7 · Closeout & acceptance

Preliminary acceptance (committee + approval) → maintenance period → final acceptance → release of final guarantee → contract closeout.

8 · Contractor evaluation

Requesting dept evaluates → Head reviews → Higher management approves → the supplier reliability index is fed.

9 · Contract signing – two scenarios

A: signed in Etimad, then imported and reflected. **B:** signed outside Etimad by creating contract data from approved drafts with manager confirmation.

10 · Contractor onboarding & invitation

After signature: single-use invitation → accept & register → bind to commercial registration and contract → Nafath & GOSI verification → access limited to their contracts only.

Full coverage: these scenarios cover the main path, execution and exceptional paths, all as gated and audited transitions.

16. FAQ

Short answers to the most frequent questions

What is the difference between Tanfeeth and Etimad?

A – Etimad handles tendering, receiving offers and award. Tanfeeth manages the entity's internal work and owns the post-signature world: contractor, payments, warnings, amendments and acceptance.

Does Tanfeeth replace Etimad?

A – No; it complements and integrates with it, and does not duplicate its official functions.

Where is the data hosted?

A – Inside Saudi Arabia, with encryption and tenant isolation, in compliance with the National Cybersecurity Authority and the Communications Authority.

How is cybersecurity ensured?

A – By complying with the Essential Cybersecurity Controls (ECC) across their four domains, under a shared responsibility between the platform, the entity and the hosting provider (section 13).

Does the AI make automatic decisions?

A – No; any financial, contractual or regulatory decision requires explicit human review and approval (the human-in-the-loop principle); the AI only suggests and explains.

How does the contractor access the platform?

A – After signature, the contracts staff send a single-use invitation; the contractor registers and the account is bound to the commercial registration and contract, with identity verified via Nafath.

What happens when a contractor defaults?

A – The system detects the delay and suggests a warning, then a final warning, then withdrawal of works if it continues, and creates a completion contract linked to the original carrying the remaining scope.

How are permissions managed?

A – Role-based access control (RBAC); the contract manager holds permanent default access to the department's orders, and assignment transfers the action permission while the manager retains access.

Does it integrate with national platforms?

A – Yes: Etimad, Nafath, the Ministry of Finance and GOSI, plus e-signature and notification channels.

Q How are official letters issued?

A – From dynamic templates with merged contract data; no external letter is sent before obtaining a reference number and date.

Q What is the difference between a “project” and a “contract”?

A – The project is the work to be delivered; the contract is the signed instrument that governs it; project execution begins after the contract is signed.

Q How long does the first phase take?

A – The reference schedule is 24 weeks; the operational core (MVP) completes around week 16, and the schedule is re-baselined after the kickoff workshop.

Q Does the system support Arabic and English?

A – Yes, with full support for Arabic (RTL) and English, the Hijri and Gregorian calendars, and the Saudi Riyal.

Q Are all actions recorded?

A – Yes, in a tamper-evident audit log that keeps the actor, time and state before and after each action.

Q What is needed before starting?

A – Settling the decisions required (section 12) and holding a kickoff workshop to approve the scope, approval chains, integration readiness and the team.

End of the main document. Appendix A – the Detailed Task Register – follows.

Appendix A – Detailed Task Register

Every task with its category, description, dependencies, status and estimated hours

This appendix breaks down the work required to deliver the platform at task level. Hours are indicative engineering estimates, refined in the kickoff workshop.

145

Total tasks

1,727

Total estimated hours


~11

person-months

Effort by category (hours)



Effort by track (hours)

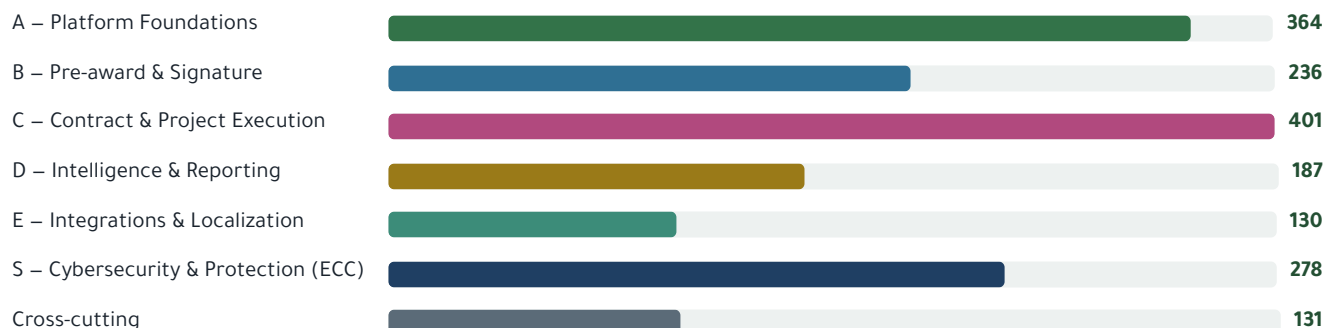

Status	Tasks	Hours
To do	138	1647
In progress	7	80
Completed	0	0

Legend:



Task Register – Track A – Platform Foundations

Track total: 364 hrs · 37 tasks

ID	Task	Category	Detailed description	Depends on	Status	Hours
E01 – Identity, Auth & RBAC – 21 hrs total						
E01.T1	CDM default-access as policy	Infrastructure	Model the contract-manager default access as a permission policy (not bespoke code): permanent access to the department orders, with the ability to act on staff behalf.	E03	In progress	7
E01.T2	Oversight & contractor permissions	Infrastructure	Add new permission keys (resource.action) for the oversight (read/audit) and contractor (own-contract only) personas to the seed catalog.	E13	To do	5
E01.T3	Rotate admin password & policy	Deployment & Ops	Rotate the seeded admin password on first boot and enforce password-strength and lockout policy.	–	To do	2
E01.T4	Auth & token-rotation tests	QA Testing	Integration tests for login, refresh-token rotation and reuse prevention, and access-token expiry.	–	In progress	7
E02 – Multi-tenancy & Data Residency – 39 hrs total						
E02.T1	Tenant context & isolation filter	Infrastructure	Request-scoped tenant context and a base repository filter scoping every query to the entity, rejecting out-of-tenant access.	E01	To do	12
E02.T2	Per-tenant file isolation	Infrastructure	Namespace and isolate file/storage paths per entity so tenants' files never overlap.	E07	To do	7
E02.T3	Cross-tenant access test	QA Testing	Automated test proving one entity cannot read another's data through any path.	E02.T1	To do	5
E02.T4	Data-residency & encryption proof	Deployment & Ops	Document and verify in-Kingdom hosting, encryption at rest/in transit, TLS and backup residency per NCA/CST.	–	To do	10
E02.T5	Tenant-scope audit & storage	Infrastructure	Scope the audit log and storage keys to the entity within multi-tenant isolation.	E04,E07	To do	5
E03 – Workflow & Business-Rules Engine – 114 hrs total						
E03.T1	Generalize the workflow engine	Infrastructure	Generalize the contract workflow slice into a reusable engine: state registry and transition definitions reused across all flows.	E01	In progress	24
E03.T2	Transition guard pipeline	Infrastructure	Per-transition guard pipeline: permission check, then business rule, then effect, then audit write.	E03.T1	To do	18
E03.T3	Standard actions & error codes	Infrastructure	Catalog of standard actions (Confirm/Reject/Return-with-comment/Edit/Assign/Comment/Sign) and unified domain error codes.	E03.T1	To do	10
E03.T4	Configurable business-rules store	Infrastructure	Configurable store for the document-split threshold (BR-01) and commencement branch (BR-02) – no hard-coding.	E03.T1	To do	12

ID	Task	Category	Detailed description	Depends on	Status	Hours
E03.T5	Configurable approval chains	Infrastructure	Configurable multi-step approval chains (delegate/escalate) per request and action type.	E03.T1	To do	12
E03.T6	Assignment & delegation	Infrastructure	Transfer action permission to the assignee while the manager retains access; assignment audited.	E01	To do	10
E03.T7	Workflow read API	Infrastructure	Workflow read API and an "available actions for me" resolver by role and state (drives UI buttons).	E03.T1	To do	7
E03.T8	Generic workflow UI	User Interface	State timeline, available-actions bar, return-with-comment modal and assignment picker.	E03.T7	To do	14
E03.T9	Gated-transition e2e	QA Testing	End-to-end test of a gated transition combining permission, rule and audit write.	E03.T2	To do	7
E04 – Immutable Audit Log – 32 hrs total						
E04.T1	Append-only audit store	Infrastructure	Audit port and append-only store written from the engine's effect step (actor, time, before/after).	E03.T1	To do	10
E04.T2	Tamper-evidence	Infrastructure	Design and initial build of a hash chain proving the audit log is tamper-evident.	E04.T1	To do	7
E04.T3	Activity timeline	User Interface	Per-contract/order activity timeline with filtering by actor, action and date.	E04.T1	To do	10
E04.T4	Audit read/export	Infrastructure	Audit-log read/export API for oversight and reporting.	E04.T1	To do	5
E05 – Correspondence, Letters & Reference Numbers – 67 hrs total						
E05.T1	Letter templates & clauses	Infrastructure	Dynamic letter templates with a versioned clause library to generate official letters.	E03	To do	14
E05.T2	Data merge & validation	Infrastructure	Merge contract/project data into templates with validation of required fields.	E05.T1	To do	7
E05.T3	PDF/Word bilingual output	Infrastructure	Render output as PDF and Word in Arabic and English, reusing the report renderer.	E05.T1	To do	10
E05.T4	Reference-number integration	Systems Integration	Integration to issue an official reference number and date via the incoming/outgoing system.	E21	To do	12
E05.T5	Reference-number gate	Infrastructure	Block any transition emitting an external letter from completing without a reference number.	E03,E05.T4	To do	5
E05.T6	Letter composer	User Interface	Edit, preview, route for signature, and show the reference badge.	E05.T1	To do	12
E05.T7	AI letter pre-fill	AI	AI pre-fills the letter with explanation; a human edits/approves before issuance.	E19	To do	7
E06 – Notifications & Task/Deadline Center – 54 hrs total						
E06.T1	Notification model & fan-out	Infrastructure	Notification model, subscription to engine events, and in-app fan-out.	E03	To do	10
E06.T2	Task & deadline center	Infrastructure	Derive tasks from open/assigned transitions with deadlines and an overdue flag.	E03	To do	10

ID	Task	Category	Detailed description	Depends on	Status	Hours
E06.T3	WhatsApp & email channels	Systems Integration	WhatsApp Business (HSM templates, opt-in/out) and email channel for external notifications.	E21	To do	10
E06.T4	Notification/task UI	User Interface	Notification center and task center UI.	E06.T1,E06.T2	To do	12
E06.T5	AI-on-behalf queue	AI	An "AI acts on my behalf" queue for routine actions, with human approval for impactful ones (later phase).	E19	To do	12
E07 – Documents, Files & E-signature – 37 hrs total						
E07.T1	Project files & status center	Infrastructure	Project files model by stage with a document status center to surface what is missing.	–	In progress	10
E07.T2	E-signature integration	Systems Integration	Provider abstraction, envelope creation, signed webhook, signed-artifact storage and audit.	–	To do	17
E07.T3	Document center UI	User Interface	Document center UI (status, by stage, upload, versions).	E07.T1	To do	10

Task Register – Track B – Pre-award & Signature

Track total: 236 hrs · 22 tasks

ID	Task	Category	Detailed description	Depends on	Status	Hours
E08 – Order Creation & Approval – 45 hrs total						
E08.T1	Order domain & Stage-1	Infrastructure	Order domain (fields, brief, attachments) and creation/approval transitions on the engine.	E03	To do	14
E08.T2	BR-01 document-split hook	Infrastructure	Apply BR-01 at budget set to split/merge the technical and financial documents.	E03.T4	To do	5
E08.T3	Optional approval gates	Infrastructure	Optional PMO, cybersecurity and local-content gates, toggleable by config.	E03	To do	7
E08.T4	Order create/approve UI	User Interface	Order create/edit screens and approval/return screens.	E03.T8	To do	14
E08.T5	Order-path tests	QA Testing	Tests for the happy path, return-with-comment and reject-with-reason.	E08.T1	To do	5
E09 – Bid-Document (Kraasa) Preparation – 24 hrs total						
E09.T1	Kraasa transitions & assignment	Infrastructure	Bid-document stage transitions and assignment to staff with action-permission transfer.	E03.T6	To do	7
E09.T2	Kraasa builder	User Interface	Bid-document builder, assignment and preview UI.	E07	To do	12
E09.T3	Kraasa output	Infrastructure	Generate the bid-document output (PDF/Word) via the correspondence/document engine.	E05,E07	To do	5
E10 – Committees: Pre-qual, Opening, Evaluation – 72 hrs total						
E10.T1	Committee models	Infrastructure	Committee models (qualification, opening, technical, examination), members, roles and workflow.	E03	To do	17
E10.T2	Scoring & committee reports	Infrastructure	Scoring/evaluation forms and committee report generation and signing.	E10.T1	To do	14
E10.T3	Pull offers from Etimad	Systems Integration	Pull offers and announcement data from Etimad and reflect them in the platform.	E21	To do	12
E10.T4	BOQ price check & comparison	Infrastructure	BOQ price-check service plus offer comparison and lowest-offer suggestion.	E10.T1	To do	12
E10.T5	Committees tab	User Interface	A dashboard per committee with score entry, reports and tracking.	E10.T1	To do	17
E11 – Announcement, Award & Letter of Intent – 44 hrs total						
E11.T1	Award & letter of intent	Infrastructure	Announcement and award transitions and generation of the award letter and letter of intent.	E10	To do	17
E11.T2	Post-qual & final commitment	Infrastructure	Post-qualification and final budget-commitment confirmation before award approval.	E03	To do	7

ID	Task	Category	Detailed description	Depends on	Status	Hours
E11.T3	Publish announcement/award	Systems Integration	Publish the announcement and award data via Etimad.	E21	To do	10
E11.T4	Announcement/award screens	User Interface	Announcement, award and letter-of-intent screens.	E11.T1	To do	10
E12 – Contract Drafting & Signature – 51 hrs total						
E12.T1	Signed-in-Etimad scenario	Infrastructure	Import the signed-contract data from Etimad and reflect it in the platform.	E21	To do	10
E12.T2	Signed-outside scenario	Infrastructure	Create contract data from approved drafts with manager confirmation.	E03	To do	10
E12.T3	Legal review & milestones	Infrastructure	Legal review and remarks path, final commitment and the milestones schedule.	E03	To do	12
E12.T4	E-sign the contract	Systems Integration	Electronically sign the contract by higher management and the contractor.	E07.T2	To do	7
E12.T5	Contract drafting screens	User Interface	Contract drafting, review and signing screens.	E12.T3	To do	12

Task Register – Track C – Contract & Project Execution

Track total: 401 hrs · 33 tasks

ID	Task	Category	Detailed description	Depends on	Status	Hours
E13 – Contractor Onboarding & Invitation – 72 hrs total						
E13.T1	Contractor account model	Infrastructure	Contractor account bound to the commercial registration and contract, scoped to entity and contract, with de-duplication.	E01,E02,E12	To do	17
E13.T2	Invitation domain	Infrastructure	Issue (signed-contract gate), single-use expiring token, accept, resend, revoke, audit.	E12,E03	To do	12
E13.T3	Identity & GOSI verification	Systems Integration	Verify contractor identity (Nafath/business identity) and GOSI compliance at onboarding.	E21	To do	14
E13.T4	Contractor permissions	Infrastructure	Contractor permission bundle scoped to their own contract actions only.	E01	To do	5
E13.T5	Invite-contractor UI	User Interface	Employee "invite contractor" flow with invitation status and resend.	E13.T2	To do	7
E13.T6	Contractor registration UI	User Interface	Contractor registration/accept flow and commercial-registration binding.	E13.T1	To do	10
E13.T7	Contractor isolation test	QA Testing	E2E: invite → accept → sees only their contract; cross-contract/tenant access denied.	E13.T1	To do	7
E14 – Contractor Portal – 72 hrs total						
E14.T1	Contractor dashboard	User Interface	Project details, timeline, performance and what is due.	E13	To do	14
E14.T2	Contract section	User Interface	Review, sign, download and share the contract.	E07.T2	To do	10
E14.T3	Contractor requests	User Interface	Contractor-initiated requests (extension/value change) entering the entity's gated workflow (BE+FE).	E16	To do	12
E14.T4	Updates window	User Interface	Updates window (text + images/video) against milestones and the BOQ (BE+FE).	E15	To do	12
E14.T5	In-platform letter replies	User Interface	In-platform replies to warning/dues/notice letters, recorded before escalation (required by the scenario).	E05,E16	To do	10
E14.T6	Contractor meetings	User Interface	Meetings tab with minutes, recording and AI summary (later phase).	E19	To do	14
E15 – Project Execution & Commencement – 93 hrs total						
E15.T1	Commencement transitions (BR-02)	Infrastructure	Commencement transitions branching by project type (supply/maintenance) with letters.	E03.T4,E05	To do	14
E15.T2	BOQ model	Infrastructure	BOQ model (item/quantity/unit price/measured/remaining) with import; feeds completion-contract carry-over.	–	To do	17
E15.T3	Milestones, progress & delay	Infrastructure	Milestones/progress model, planned-vs-actual and delay computation.	E15.T2	To do	12
E15.T4	Payments (mustakhlasad)	Infrastructure	Payments against the BOQ and MoF budget availability, gated and audited.	E15.T2,E21	To do	14

ID	Task	Category	Detailed description	Depends on	Status	Hours
E15.T5	Project execution dashboard	User Interface	Execution dashboard (timeline, milestones, BOQ progress, delay flags, payments).	E15.T3	To do	19
E15.T6	Commencement/site-handover UI	User Interface	Commencement, site-handover-minute and cover-letter screens.	E15.T1	To do	10
E15.T7	Commencement tests	QA Testing	Tests for supply and maintenance commencement with the site-handover committee.	E15.T1	To do	7
E16 – Contract Lifecycle Actions (18) – 101 hrs total						
E16.T1	Action framework on the engine	Infrastructure	Trigger + precondition rule + owner role + approval chain + letter template + state/financial/guarantee effect + AI-suggestion hook.	E03.T1,E05	To do	24
E16.T2	MVP action set	Infrastructure	Eight MVP actions (commence, warning, final warning, withdrawal, variation, extension, suspension, resumption) as config rows.	E16.T1	To do	19
E16.T3	Phase-2 action set	Infrastructure	Dues, assignment, labor endorsement, preliminary/final acceptance, termination, guarantees, representative delegation.	E16.T1,E18,E13	To do	22
E16.T4	AI suggestion per action	AI	AI suggestion and explanation per action under human oversight.	E19	To do	12
E16.T5	Action launcher UI	User Interface	Action launcher on the contract/project view with letter preview, approval and signing.	E03.T8,E05.T1	To do	14
E16.T6	Action e2e tests	QA Testing	E2E per action group (permission + rule + letter + reference + audit + state).	E16.T2	To do	10
E17 – Contract Linking & Completion Contracts – 34 hrs total						
E17.T1	Contract relationship model	Infrastructure	Typed contract-relationship links shown on both contracts.	E16	To do	10
E17.T2	Completion-contract spawn	Infrastructure	Spawn the completion contract from withdrawal, carrying the remaining BOQ and linking to the original.	E16,E15.T2	To do	12
E17.T3	Linked-contracts UI	User Interface	Linked-contracts UI and original↔completion chain view.	E17.T1	To do	7
E17.T4	Completion e2e test	QA Testing	E2E: withdrawal → linked completion contract with the remaining scope.	E17.T2	To do	5
E18 – Closeout & Contractor Evaluation – 29 hrs total						
E18.T1	Acceptance transitions	Infrastructure	Preliminary/final acceptance transitions with committee and higher-management approval.	E16	To do	12
E18.T2	Guarantee release & closeout	Infrastructure	Release the final guarantee and close the contract.	E18.T1	To do	7
E18.T3	Contractor evaluation	Infrastructure	Contractor evaluation form feeding the supplier reliability index (BE+FE).	E20	To do	10

Task Register – Track D – Intelligence & Reporting

Track total: 187 hrs · 14 tasks

ID	Task	Category	Detailed description	Depends on	Status	Hours
E19 – AI Layer & HITL – 116 hrs total						
E19.T1	Recommendation & approval domain	Infrastructure	A recommendation object (recommendation + rationale + confidence + sources) with a human decision recorded in the audit log.	E04	To do	12
E19.T2	Next-Best-Action engine	AI	Engine recommending the next action over contract/project state with justification.	E03,E15	In progress	17
E19.T3	Risk-scoring service	AI	Risk scoring (delay/financial/compliance) with drivers, feeding the risk heatmap.	E15	To do	17
E19.T4	Clause/compliance scanner	AI	Scan contracts/letters for missing mandatory clauses and deviations.	E05,E12	To do	14
E19.T5	Knowledge assistant	AI	Assistant and contextual search over rules, the procurement law and each contract.	–	To do	17
E19.T6	Fraud/collusion/COI detection	AI	Bid-collusion, financial-anomaly and conflict-of-interest detection – advisory under oversight (later phase).	–	To do	24
E19.T7	Rate limit & AI opt-in	Infrastructure	AI call rate limit and a per-tenant AI enablement flag.	–	In progress	5
E19.T8	HITL approval surface	User Interface	UI showing the recommendation and its explanation with approve/edit/reject.	E19.T1	To do	10
E20 – Dashboards & Reporting – 71 hrs total						
E20.T1	CDM dashboard	User Interface	Contract-manager dashboard: performance, contracts summary with color-coded alerts, repository and lifecycle tracker.	E15,E16,E04	To do	17
E20.T2	Executive dashboard	User Interface	Higher-management strategic dashboard with the risk heatmap.	E19	To do	17
E20.T3	End-user dashboard	User Interface	End-user dashboard: projects, pending requests, document status and timeline.	–	To do	10
E20.T4	Oversight/compliance view	User Interface	Compliance and audit-log view for oversight bodies.	E04	To do	10
E20.T5	Report generator extension	Infrastructure	Extend the report generator and executive summary (built on the existing engine).	–	In progress	10
E20.T6	Supplier reliability index	Infrastructure	Aggregate the supplier reliability index from contractor evaluations and performance.	E18	To do	7

Task Register – Track E – Integrations & Localization

Track total: 130 hrs · 9 tasks

ID	Task	Category	Detailed description	Depends on	Status	Hours
E21 – National Integrations – 87 hrs total						
E21.T1	Etimad adapter	Systems Integration	Etimad adapter (publish/offers/payments) behind a domain port with sync/reconciliation jobs.	E02	To do	24
E21.T2	Nafath adapter	Systems Integration	Nafath adapter for identity and authentication.	E02	To do	12
E21.T3	MoF adapter	Systems Integration	Ministry of Finance adapter (budget, bid examination, payment plans).	E02	To do	17
E21.T4	GOSI adapter	Systems Integration	GOSI adapter for supplier-compliance verification.	E02	To do	10
E21.T5	Supporting adapters	Systems Integration	E-signature, ERP/CRM and WhatsApp (sync/notifications).	E02	To do	14
E21.T6	Integration sandboxes	Deployment & Ops	Sandboxes and contract tests for integrations during development before live links.	–	To do	10
E22 – Vision 2030 & Localization – 43 hrs total						
E22.T1	Localization dashboard	User Interface	Localization dashboard, local-content index and Nitaqat/Saudization.	E20,E21	To do	17
E22.T2	Zakat & VAT automation	Infrastructure	Zakat and VAT automation in the related accounts.	–	To do	12
E22.T3	Mega-project risk & Arabic NLP	AI	Mega-project risk analysis and Arabic NLP.	–	To do	14

Task Register – Track S – Cybersecurity & Protection (ECC)

Track total: 278 hrs · 24 tasks

ID	Task	Category	Detailed description	Depends on	Status	Hours
Cybersecurity Governance (ECC-1) – 67 hrs total						
S1.T1	Cybersecurity strategy & policy	Security	Define, document and approve the platform cybersecurity strategy, policies and procedures and publish to stakeholders (ECC 1-1/1-3).	–	To do	17
S1.T2	Roles & governance	Security	Define cybersecurity roles and responsibilities (RACI) and the governance/oversight framework (ECC 1-4).	–	To do	7
S1.T3	Cyber risk management	Security	Risk methodology and register, with assessment in IT-project phases, before major changes and for third-party services (ECC 1-5/1-6).	–	To do	14
S1.T4	Compliance & periodic audit	Security	Compliance with legal/regulatory requirements and periodic self-assessment/audit against the controls (ECC 1-7/1-8).	–	To do	12
S1.T5	Cybersecurity in HR	Security	Confidentiality clauses, security screening for sensitive roles, and pre/during/post-employment requirements (ECC 1-9).	–	To do	10
S1.T6	Awareness & training	Security	Periodic awareness program (phishing, devices, social media) and specialized training for technical teams (ECC 1-10).	–	To do	7
Cybersecurity Defense (ECC-2) – 177 hrs total						
S2.T1	Identity hardening (MFA/PAM)	Security	MFA for sensitive accounts and remote access, privileged-access management, least privilege and segregation of duties (ECC 2-2); extends E01.	E01	To do	14
S2.T2	Cryptography & key management	Security	Encryption by classification at rest/in transit and key-lifecycle management per NCA standards (ECC 2-8); extends E02.	E02	To do	14
S2.T3	Systems & endpoint protection	Security	Anti-malware, patch management, configuration hardening and clock synchronization (ECC 2-3).	–	To do	12
S2.T4	Email protection	Security	Phishing/spam filtering, SPF/DKIM/DMARC and APT protection (ECC 2-4).	E06	To do	10
S2.T5	Network security (Firewall/IPS/DDoS)	Security	Segmentation and defense-in-depth, firewalls, IPS, DDoS protection, DNS security and production isolation (ECC 2-5).	–	To do	17
S2.T6	Mobile & BYOD security	Security	Separate entity data on personal devices and remote-wipe on loss or end of relationship (ECC 2-6).	–	To do	7
S2.T7	Data protection by classification	Security	Data classification and DLP/masking controls by sensitivity level (ECC 2-7); extends E02.	E02	To do	10

ID	Task	Category	Detailed description	Depends on	Status	Hours
S2.T8	Backup & restore testing	Security	Backup coverage of sensitive assets, fast recovery and periodic restore testing (ECC 2-9).	–	To do	7
S2.T9	Vulnerability management	Security	Periodic scanning, classification, remediation, pre-production verification and advisory subscriptions (ECC 2-10).	–	To do	12
S2.T10	Penetration testing	Security	Periodic penetration testing of external services, websites, web/mobile apps and remote access (ECC 2-11).	–	To do	12
S2.T11	Event logs & monitoring (SIEM)	Security	Event-log collection and continuous monitoring via SIEM, retained ≥12 months (ECC 2-12); builds on E04.	E04	To do	17
S2.T12	Incident management (IR)	Security	Response plans, incident classification, reporting to the authority and threat intelligence (ECC 2-13).	–	To do	14
S2.T13	Physical security	Security	Access control and CCTV for sensitive areas – largely via the hosting provider (ECC 2-14).	E21	To do	5
S2.T14	Web application protection (WAF)	Security	Web application firewall, multi-tier architecture, HTTPS and a secure session policy (ECC 2-15).	–	To do	12
S2.T15	Secure SDLC	Security	Secure coding standards, trusted libraries, security testing and configuration hardening before release (ECC 1-6).	–	To do	14
Cybersecurity Resilience (ECC-3) – 12 hrs total						
S3.T1	Resilience in BCM	Security	Embed cybersecurity in business continuity: RTO/RPO objectives, recovery plan and testing (ECC 3-1).	–	To do	12
Third-Party & Cloud Computing (ECC-4) – 22 hrs total						
S4.T1	Third-party security	Security	Contractual requirements and cyber assessment of suppliers/third parties before and during engagement (ECC 4-1).	–	To do	10
S4.T2	Cloud & hosting security	Security	In-Kingdom data residency, shared-responsibility model and cloud-configuration hardening (ECC 4-2); extends E02.	E02	To do	12

Task Register – Cross-cutting (QA, Ops, Design, PM)

Track total: 131 hrs · 6 tasks

ID	Task	Category	Detailed description	Depends on	Status	Hours
Cross-cutting tasks – 131 hrs total						
X.QA1	Automated test framework	QA Testing	Automated test framework (unit + e2e) across modules covering transitions, permissions and audit.	–	To do	24
X.OPS1	CI/CD & environments	Deployment & Ops	CI/CD pipelines, runtime environments (staging/production) and monitoring.	–	To do	19
X.OPS2	Backup & disaster recovery	Deployment & Ops	Backup, disaster recovery, monitoring and alerting.	–	To do	14
X.UX1	Design system & i18n	Design	Design system, RTL components and translation files (Arabic/English) for all modules.	–	To do	24
X.PM1	Project management & workshops	PM	Project management, decision workshops, requirements documentation and traceability throughout delivery.	–	To do	36
X.DOC1	Architecture docs & training	PM	Architecture documentation, user guides and training.	–	To do	14
